

Hi there,

Before we proceed, I want to clearly align on how this project needs to run to meet the March deadline without introducing accounting or valuation risks.

I will be working 6–8 focused hours per day on this implementation. To move at this pace safely, I'll need:

One clear decision-maker on your side

Daily availability for reviews/decisions (2–4 hours across key stakeholders)

Agreement that core foundations (UoMs, valuation, accounting, stock rules) are locked early and not revisited casually

The main setbacks that impact timeline are delayed decisions, late scope changes, and incomplete data during migration. When these happen, accounting and valuation integrity—not just timelines—are what get compromised, which I will actively avoid.

My hourly rate is USD 42 (slightly negotiable).

Based on similar projects, the total effort is realistically 210–250 hours, depending on data quality, user readiness, and scope stability.

To manage risk and progress, I recommend:

Daily milestones that are clearly defined, reviewed, and signed off, or

A weekly retainer, paid in advance, which allows continuous execution without administrative delays.

I'm happy to discuss which engagement model works best for you, but payment must be confirmed before work begins so momentum isn't lost.

Looking forward to aligning on this and moving forward efficiently.

Odoo ERP Implementation – Weekly Plan & Daily Checklist

Week 1 – Foundation & Lockdown

Weekly Objectives:

- - Review functional specification
- - Confirm scope, timeline, and roles
- - Set up Odoo instance
- - Configure companies, currencies, users, access rights
- - Define and LOCK: UoMs, valuation method (FIFO), taxes, accounts
- - Confirm migration scope and cutover approach

Week 2 – Accounting & Stock Core

Weekly Objectives:

- - Chart of accounts configuration
- - VAT rules and fiscal positions
- - Stock valuation accounts
- - Landed cost workflow setup
- - Test receive → value → post flow

Week 3 – Manufacturing (Process)

Weekly Objectives:

- - Process BOMs
- - UoM conversions (kg ↔ liter)
- - Waste & by-products
- - Lot traceability
- - Production testing

Week 4 – Migration (QuickBooks)

Weekly Objectives:

- - Export QBO data
- - Map accounts, customers, vendors, products
- - Import opening balances
- - Reconciliation checks

Week 5 – Field Service & Reporting


Weekly Objectives:

- - Field Service workflows
- - Custom mobile forms (Studio)
- - PDF reports
- - WhatsApp integration testing

Week 6 – UAT, Training & Go-Live

Weekly Objectives:

- - User Acceptance Testing
- - Staff training
- - Final migration
- - Go-live

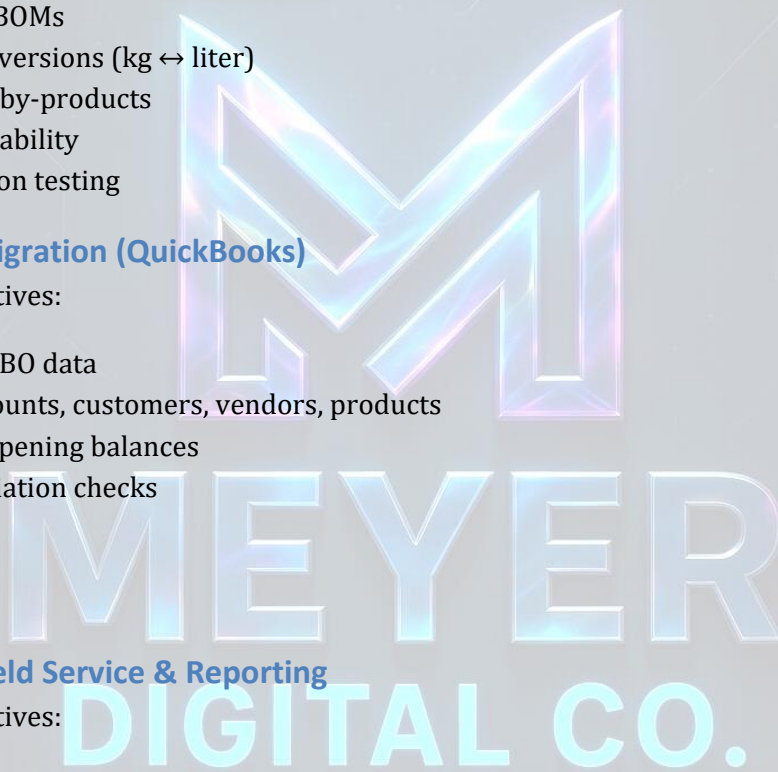

- - Stabilization

ODOO ERP IMPLEMENTATION

Exact Day-by-Day Checklist

WEEK 1 – FOUNDATIONS (NON-NEGOTIABLE)

Goal: Lock anything that can break accounting or stock. No UI polish.

Day 1 – Project Lockdown

- Read full functional spec end-to-end
- Identify:
 - Valuation method (FIFO confirmed)
 - Base UoMs (kg base)
 - Companies, currencies
- Define **scope freeze list**
- Define **out-of-scope list**
- Confirm:
 - Single decision maker
 - Go-live date
- Create decision log

Outcome: No ambiguity on “who decides what”

Day 2 – Odoo Instance & Core Settings

- Install Odoo (Enterprise/Community as agreed)
- Enable core apps:
 - Accounting
 - Inventory
 - Manufacturing
 - Sales
 - Purchase
 - Field Service
 - Project
- Configure:
 - Companies
 - Multi-currency
 - User roles (admin vs operations)
- Disable anything not needed

Outcome: Clean base system

Day 3 – Accounting Skeleton

- Configure:
 - Fiscal country = South Africa
 - VAT 15%, zero-rated, exempt
 - Tax groups
- Build Chart of Accounts
- Configure:
 - Stock valuation accounts
 - Expense / income accounts
- Lock:
 - No account editing for ops users

Outcome: Accounting cannot drift later

Day 4 – Inventory & Valuation Lock

- Configure:
 - FIFO valuation
 - Real-time valuation
- Create UoM categories:
 - Weight (kg base)
 - Volume (liter secondary)
- Lock:
 - No negative stock
 - No backdating for warehouse users
- Configure landed cost accounts

Outcome: SVLs protected

Day 5 – Manufacturing Rules

- Enable:
 - Lots / serials
 - By-products
 - Work orders (if needed)
- Define:
 - Process BOM rules
 - Waste handling method
- Decide:

- Fixed vs batch density

- Document “**never do**” rules

Outcome: Manufacturing can’t bypass valuation

WEEK 2 – FINANCE + STOCK VALIDATION

Day 6 – Landed Cost Flow

- Configure landed cost products:

- Freight
 - Duties
- Test:
 - Receipt → landed cost → valuation
- Test failure case:
 - Consume before landed cost
- Document operational rule

Outcome: Imports won't corrupt COGS

Day 7 – End-to-End Stock Test

- Receive raw material
- Apply landed cost
- Consume via MO
- Produce finished goods
- Sell & invoice
- Validate:
 - Stock valuation layers
 - Journal entries

Outcome: One clean golden flow

Day 8 – Permissions & Guardrails

- Lock:
 - Stock adjustments
 - Backdating
 - Manual valuation edits
 - Simplify warehouse screens
 - Test as warehouse user
- Outcome: Old-school users can't break system

Day 9 – Reporting Sanity Check

- Stock valuation report
- Inventory aging
- P&L vs stock movements
- Confirm numbers make sense

Outcome: Finance trusts numbers

Day 10 – Foundation Freeze

- Review all locked decisions
- Get written sign-off
- Freeze:
 - UoMs
 - Valuation
 - Accounts

- Taxes

No changes after this without impact analysis

WEEK 3 – MANUFACTURING CONFIG

Day 11 – Product Master Data

- Create raw materials
- Create finished goods
- Assign:
 - UoMs
 - Valuation
 - Lots
- No prices yet (migration later)

Day 12 – Process BOMs

- Build core BOMs
- Add:
 - By-products
 - Waste
- Validate quantities

Day 13 – Manufacturing Testing

- Run test MO
- Validate:
 - Consumption
 - Yield
 - Valuation layers
- Fix rounding issues

Day 14 – Edge Cases

- Partial production
- Rework scenario
- Scrap scenario
- Document allowed vs forbidden actions

Day 15 – Manufacturing Sign-off

- Demo to operations
- Get approval
- Freeze BOM logic

WEEK 4 – QUICKBOOKS MIGRATION

Day 16 – QBO Data Audit

- Export:
 - COA

- Customers
 - Vendors
 - Products
 - AR/AP
- Identify:
 - Junk data
 - Non-migratable items

Day 17 – Master Data Import

- Import:
 - Customers
 - Vendors
 - Products
- Validate mappings

Day 18 – Opening Balances

- Import opening trial balance
 - Import open AR/AP
 - Reconcile differences
- Do NOT proceed until balanced**

Day 19 – Stock Opening

- Import stock quantities by lot
- Validate valuation vs QBO
- Fix discrepancies

Day 20 – Migration Validation

- Balance sheet matches QBO
- AR/AP matches
- Stock valuation signed off

WEEK 5 – FIELD SERVICE + REPORTING

Day 21 – Field Service Setup

- Configure:
 - Teams
 - Task flow
 - Verify → bill logic

Day 22 – Mobile Forms (Studio)

- Build water quality form
- Add:
 - TDS

- pH
 - Test on mobile
-

Day 23 – PDFs & Graphs

- Build PDF report
- Add charts
- Test auto-generation

Day 24 – WhatsApp Integration

- Configure API
- Send test PDFs
- Log failures

Day 25 – Field Service UAT

- Offline test
- Sync test
- Billing verification

WEEK 6 – UAT, TRAINING, GO-LIVE

Day 26 – User Training

- Finance
- Warehouse
- Field techs
- Emphasize “do not break” rules

Day 27 – Full UAT

- Real scenarios
- Log blockers
- Fix only critical issues

Day 28 – Final Migration

- Freeze QBO
- Re-import final balances
- Final reconciliation

Day 29 – Go-Live

- Monitor:
 - Stock moves
 - Invoices
 - Field sync
 - Same-day fixes only
-

Day 30 – Stabilization

- Review SVLs
 - Review journals
 - Address user errors
 - Lock system
-

